

CLARENDON RESIDENT MEETING AUGUST 26, 2024

### **Introductions**

- Interpretation Needs (In person and Virtual)
- Clarendon Residents United + Legal
- Dellbrook Construction
- Somerville Housing Authority
- Housing Opportunities Unlimited
- POAH & SCC

## Construction Updates

- Modular boxes started arriving in May. Level 3's stacking is ongoing. Expected completion of stacking modules in early January.
- Larger crane is in use as of 8/19. Breaking down the crane will have the same impact to parking when stacking is complete towards the end of the project.
- Framing of the amenity space is ongoing, which includes the lobby and residential lounge, mailroom and package area, offices, and community room.
   Plumbing, electrical, and HVAC work in the amenity space has started.
- Residents moving into Building E will be contacted towards the end of the year to prepare for lease-up.



### **Construction Timeline**

- Demolition: 6 weeks (mid-May 23)
- Site & Foundations: 6 months (May-Nov 23)
- Concrete and Steel Podium: 5 months (Nov 23-April 24)
- Stacking of modular boxes: 7 months (June 24-Jan 25)
- Vertical construction: 14 months (Jan 24-March 25)
- Finish site work & landscaping: 8 months (July 24-March 25)
- Expected Completion: March 25
- Residential lease-up: 3 months (April-June 25)

#### **Construction Reminders**

• Job applications available on the site fence

• Security cameras are live. Notices go to the construction team and


police if someone trespasses

Want construction updates?

Text: CLARENDONHILL to 8447642012 to join our list



### **Building E Amenity Space Overview**

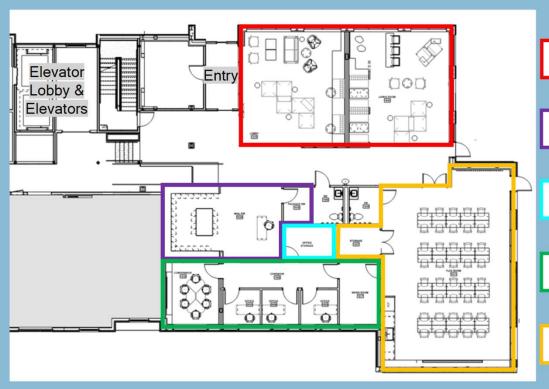

Lobby & Residential Lounge

Mailroom and Package Area

**CRU Office** 

**Management Offices** 

Community Room

## Phase 2: Park or Parking?



## Phase 2: Park or Parking?



## **Upcoming Events**

- Next Construction Resident Meeting: Monday September 16<sup>th</sup> at 6:30pm
- **HOU is on site** Monday Friday between 8:00AM and 4:00PM
- SCC is on site September 18<sup>th</sup> 9:00 to 11:00AM







### **Economic Opportunity**









#### **Scan this QR code for:**

- The Fist Source Jobs Program
- One-on-one Financial Literacy
- Learn how to buy a home
- Digital Literacy Classes



# Watch the work happen!

https://app.oxblue.com/?openlink=poah/clarendon



#### **Questions? Please contact:**

CRU: ClarendonResidentsUnited@gmail.com

Developers: mmiller@poah.org or asolis@somervillecdc.org

Relocation Specialist: <u>kmarsh@housingopportunities.com</u> 617-344-9616

**Construction Page:** 

https://clarendonhill.org/resident-info/construction-updates/

#### MISC./REFERENCE SLIDES

### Re-Occupancy, Relocation, and Phase 2 Updates

- Phase 2a funding has been received!
- As we near construction completion and prepare for Phase 2a, families will either move into the new building or move off site.
- HOU is working with residents eligible for 3BR units to plan for upcoming moves.
- HOU is on site Monday Friday 8AM to 4PM to answer any relocation questions.
- SCC will be on site September 18<sup>th</sup> 9:00 to 11:00AM.



Phase I – Under construction


Phase 2a – Construction to begin after Phase I

Phase 2b – On hold

### Re-Occupancy Overview

- 1. Any household relocated off-site who received a notice to quit in a no-fault eviction
- 2. Priority households who are currently living in Phase II and had already moved once (Phase I relocatees)
- 3. Priority households who moved off site
- 4. Priority households who remained in place in Phase II buildings (Phase II priority households)
- 5. Non-priority households living in Phase II
- 6. Non-priority households relocated off-site

#### 1-bedroom layouts







1 UNIT TYPE 1A - (1BR TYP.)

2-bedroom layouts (Slide 1 of 2)





2-bedroom layouts (Slide 1 of 2)





2-bedroom layouts (Slide 2 of 2)




1 UNIT TYPE 2A - (TYPICAL 2BR)



3 UNIT TYPE 2D - (2BR GROUP 2)

3-bedroom layouts







UNIT TYPE 3A - (TYP. 3BR CORNER-GROUP 1)
